EPC Wind Project – Power BI Dashboard Concept (3 Sites)

From Land to Clean Energy – On Time, On Track, Together

1 Executive Command Center

Last Refresh: 15 Jan 2025


Executive | Portfolio | WTG | Commissioning | PSS | Transmission | Financial | Map | Risk | Assets


Select Site: All Sites, Site Alpha, Site Beta, Site Gamma
State: All
Date: Jan 2025

Overall Project Progress	WTG Progress	PSS Progress	Transmission Progress	Commissioning Readiness
68%	72%	65%	58%	42%
+5% vs last month	+6%	+4%	+8%	+10%

Total Capacity	WTGs	PSS	33 kV Lines	Sites
450 MW	75 (48 Installed)	3 (2 in Progress)	120 km (70 km Complete)	3 (1 On Track)







Key Highlights
- Site Alpha ahead of schedule
- WTG erection pace improved by 15%
- PSS civil works 80% complete at Site Beta

Top 3 Concerns
- Transmission delay at Site Gamma
- PSS equipment delivery risk
- Land clearance pending for 5 WTGs

Next 30 Days Focus
- Complete PSS testing at Site Alpha
- Accelerate stringing at Site Beta
- Clear land & RFC for pending WTGs

2 Portfolio Health Dashboard

Last Refresh: 15 Jan 2025

Executive | Portfolio | WTG | Commissioning | PSS | Transmission | Financial | Map | Risk | Assets

Select Site: All Sites, Site Alpha, Site Beta, Site Gamma
State: All
Date: Jan 2025

Sites On Track	Sites Delayed	Total Capacity	Budget Utilization
1/3	2/3	450 MW	62%





Site Summary

Site	State	Capacity (MW)	Progress %	Delay (Days)	Budget (₹ Cr)	Actual (₹ Cr)	Status
Site Alpha	Tamil Nadu	200	82%	5	320	210	On Track
Site Beta	Gujarat	150	61%	28	250	180	At Risk
Site Gamma	Rajasthan	100	46%	65	180	120	Delayed

3 WTG Construction Dashboard

Last Refresh: 15 Jan 2025


Executive | Portfolio | WTG | Commissioning | PSS | Transmission | Financial | Map | Risk | Assets


Select Site: All Sites, Site Alpha, Site Beta, Site Gamma
State: All
Date: Jan 2025

Land Acquired	RFC	Foundation	RFE	Pathway	WTG Erection
95%	88%	76%	68%	72%	65%









WTG Backlog

RFC	5
Foundation	8
RFE	10
Pathway	12
Erection	15

4 WTG Readiness & Commissioning

Executive | Portfolio | WTG | Commissioning | PSS | Transmission | Financial | Map | Risk | Assets

Select Site: All Sites, Site Alpha, Site Beta, Site Gamma
State: All
Date: Jan 2025

MCC	Pre-Commissioning	Quality Audit	Ready for Charging	Connected to PSS
52%	42%	38%	32%	28%







WTG Exception List


WTG ID	Site	Current Stage	Delay (Days)
WTG-027	Site Beta	Foundation	28
WTG-041	Site Gamma	RFE	45
WTG-055	Site Gamma	Erection	60
WTG-063	Site Beta	Pre-Comm	32
WTG-071	Site Alpha	QA	20

5 PSS Construction Dashboard

Executive | Portfolio | WTG | Commissioning | PSS | Transmission | Financial | Map | Risk | Assets

Select Site: All Sites, Site Alpha, Site Beta, Site Gamma
State: All
Date: Jan 2025

Civil	Equipment Installation	Cable Work	Testing	Ready for Charging
78%	65%	52%	38%	30%







Critical PSS Activities

Site	Activity	Progress %	Remarks
Site Alpha	Testing	60%	On track
Site Beta	Cable Work	40%	Delayed
Site Alpha	Equipment Install	20%	Material pending

6 Transmission (33 kV) Dashboard


Executive | Portfolio | WTG | Commissioning | PSS | Transmission | Financial | Map | Risk | Assets

Select Site: All Sites, Site Alpha, Site Beta, Site Gamma
State: All
Date: Jan 2025

ROW Cleared	Pole Erection	Stringing	OPGW
82%	68%	55%	42%







Pending Sections

Feeder	Section	Pending (km)	Status
Panther	P1–P5	12	Delayed
Panther	P6–P8	8	In Progress
Dog	D1–D4	10	Delayed
Dog	D5–D7	5	In Progress

7 Financial & Capacity Dashboard

Executive | Portfolio | WTG | Commissioning | PSS | Transmission | Financial | Map | Risk | Assets

Select Site: All Sites, Site Alpha, Site Beta, Site Gamma
State: All
Date: Jan 2025

Total Budget	Actual Spend	Variance	Cost per MW
₹ 750 Cr	₹ 510 Cr	₹ 240 Cr	₹ 1.70 Cr








Financial Summary

Site	Budget	Actual	Variance	Utilization %
Site Alpha	320	210	110	66%
Site Beta	250	180	70	72%
Site Gamma	180	120	60	67%
Total	750	510	240	68%

8 Geographic Intelligence

Executive | Portfolio | WTG | Commissioning | PSS | Transmission | Financial | Map | Map | Risk | Assets

Select Site: All Sites, Site Alpha, Site Beta, Site Gamma
Map View: Sites, WTGs
Layer: Progress, Capacity

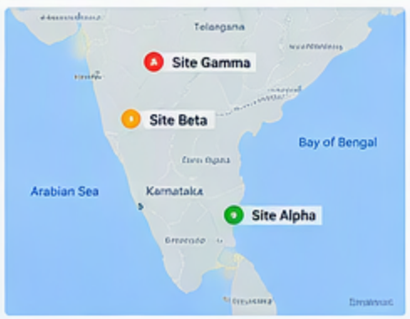

Site Details

Site	State	Capacity (MW)	Progress %
Site Alpha	Tamil Nadu	200	82%
Site Beta	Gujarat	150	61%
Site Gamma	Rajasthan	100	46%


WTG Locations (Site Alpha)



Erected
In Progress
Not Started

9 Risk & Bottleneck Analytics

Total Risks	High Risks	At Risk Capacity	Avg Delay
12	5	95 MW	32 Days





Risk Register (Top 5)

Risk ID	Site	Category	Description	Impact	Status
R-001	Site Gamma	Land	Land clearance pending for 5 WTGs	High	Open
R-002	Site Beta	Supply Chain	PSS equipment delay	High	Open
R-003	Site Gamma	Transmission	Stringing delay (D1–D4)	Medium	Open
R-004	Site Beta	Weather	Heavy rains affecting civil works	Medium	Monitoring
R-005	Site Alpha	Grid	Testing approval pending	Medium	Monitoring

10 Asset / WTG Drill-Through

Executive | Portfolio | WTG | Commissioning | Commissioning | Transmission | Financial | Map | Risk | Assets

Select Site: All
Select Feeder: All
Select OEM: All
Select Turbine Model: All

Total Assets	Erected	Ready for Charging	Connected to PSS
75	48	24	21

WTG Asset Details

Asset ID	WTG ID	Site	Feeder	OEM	Model	Current Stage	GPS Location
A-001	WTG-001	Site Alpha	Panther	Vestas	V162	Erected	
A-002	WTG-002	Site Alpha	Panther	Vestas	V162	Pre-Comm	
A-003	WTG-003	Site Beta	Dog	GE	3.4	Foundation	
A-004	WTG-004	Site Beta	Dog	GE	3.4	RFE	
A-005	WTG-005	Site Gamma	Panther	Suzlon	S144	Not Started	
...	...	...	...	...	...	...	

WTG Progress Timeline (WTG-001)

Land ✓ — RFC ✓ — Foundation ✓ — RFE ✓ — Pathway ✓ — Erection ✓ — MCC ✓ — Pre-Comm ✓ — QA ✓ — Charging ✓
